




[Current Status]

- Started DAT October 24, 2007
 - Built 10 Model 770's in 30-06 for function test
 - Awaiting delivery of five .243 Win and five 7mm-08 for drop testing
 - Start of DAT was delayed 1 month due to ordering additional fire controls and issues with the receiver insert

Continued on Page 3

[Design Activity]

- Redesign of receiver insert due to trigger pull adjustment screw backing out
- Redesigned safety arm with integrated button

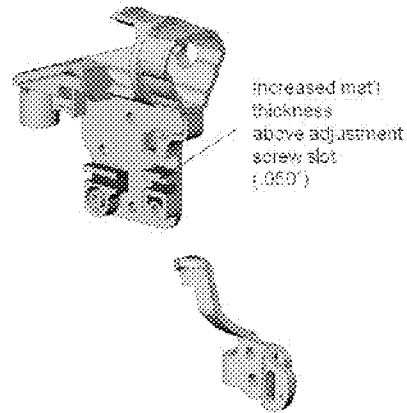

Continued on Page 2

[Action Items]

Action Item	Status	Responsible	Due Date
Complete DAT	In process	Test Lab	11/2/07

Continued on Page 2
Remington Arms Company, Inc.

[Schedule]

- DAT (20 guns)
 - Complete DAT – November 2, 2007
(revised from October 12, 2007)

Continued on next page
