


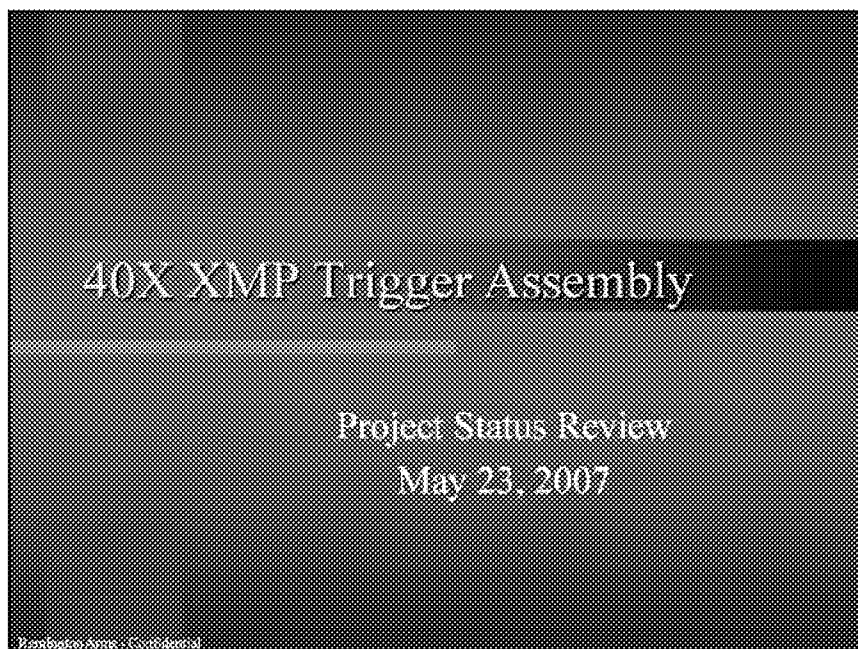

40X XMP TA Action Items

Action Item	Status	Responsible	Date
Conduct XR-100 DAT	Complete	R&D Test Lab	4/13/2007
Check and release drawing package for T&P	Complete	Ronkainen	4/24/2007
Conduct FET on 700 Varmint	Complete	Ronkainen	5/16/2007
Get parts for 700 Varmint DAT	In process	Ronkainen	5/13/2007
Conduct DAT on 700 Varmint	Pending	R&D Test Lab	7/11/2007

Remington Arms - Confidential

40X XMP Status

- XR-100 DAT successfully completed
- Drawing package reviewed & released for T&P
- NPP issued by marketing
- *Just when you thought you were done...*
 - Marketing would like 40X XMP across M/700 Varmint lines
 - Successful EET for 40X XMP on M/700 Varmint for SAAMI Jar-Off, Rotation, and Drop tests
 - New DAT scheduled for 40X XMP on M/700 Varmint line
 - DAT will tentatively only include SAAMI Jar-Off/Rotation /Drop testing and 40 lb Trigger test

Remington Arms - Confidential

40X XMP Summarized Schedule

Milestone	Date
First non-working prototype	N/A
First working prototype	N/A
EET	10/15/2006
Manufacturing involvement	3/14/2005
XR-100 DAT	4/13/2007
M/700 Varmint DAT	7/11/2007

Remington Arms - Confidential
