




## [ Status ]

- Started DAT October 24
  - Built 10 Model 770's in 30-06 for function testing. Function testing complete
  - Built 5 each in .243 WIN and 7mm REM MAG for drop testing. Drop testing complete
  - Total DAT approximately 90% completed
  - No "show stoppers" to date

Revised: 10/25/00  
Remington Arms Company, Inc.

## [ Design Activity ]

- Redesign of receiver insert due to trigger pull adjustment screw backing out
- Redesigned safety arm with integrated button for possible cost reduction

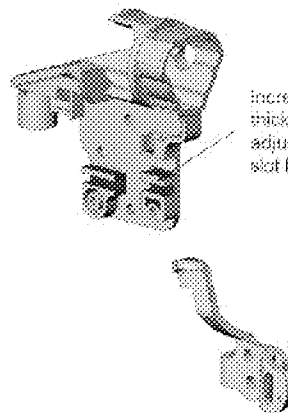

Revised 04/2000  
Remington-Union Metallic

## [ Action Items ]

Action Item	Status	Responsible	Due Date
Write CAR	Completed	Mayfield	10/26/07
Complete DAT	In process	Test Lab	11/16/07 (revised from 11/9)
Summarize DAT and write report	In process	Test Lab/Norton	11/20/07
Provide schedule for production implementation	Pending completion of DAT	Mayfield	11/23/07

Revised 11/16/07  
Remington Arms Company, Inc.

## [ Schedule ]

- DAT (20 guns)
  - November 9, 2007 (revised from October 12, 2007)
- Submit CAR for approval
  - November 9, 2007 (Submittal upon completion of DAT)

Revised 10/12/07  
Remington Arms Company
