



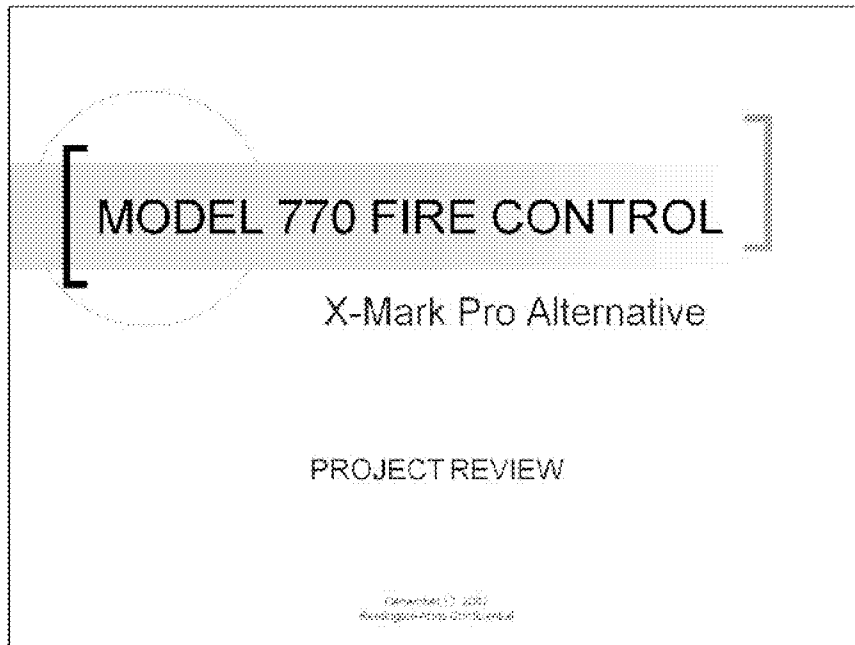

X-Mark Pro Alternative

PROJECT REVIEW

Generated: 12/2021
Revised: 12/2021

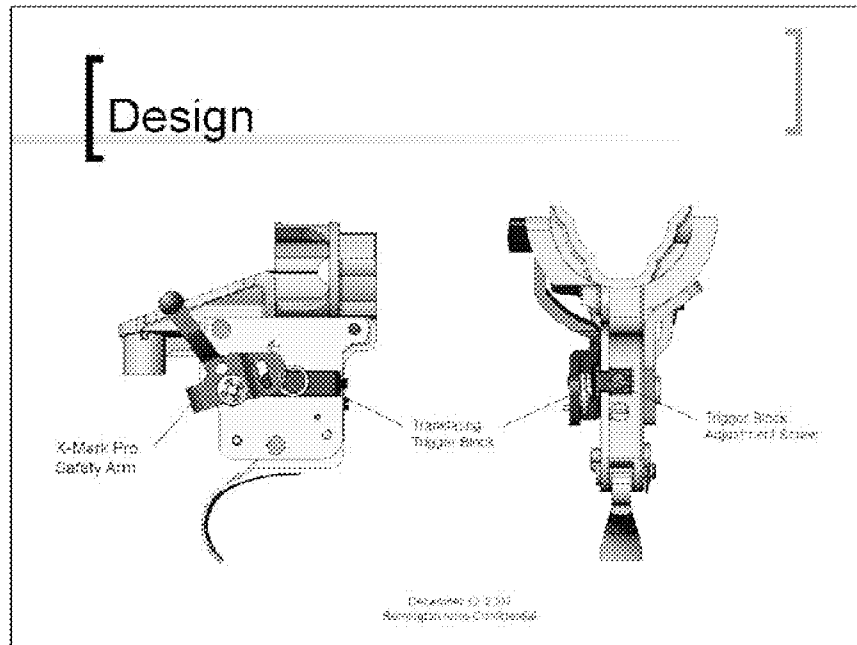

[Status]

- DAT Completed November 16
 - 20 Model 770's tested
 - Function testing of 10 Model 770's in 30-06
 - Drop testing of 5 each .243 WIN and 7mm REM MAG
 - DAT was successful and moving forward with production tooling build
 - Complete DAT results in attachment
 - Click on icon to view



Document ID: 12345
Remington Arms Company, Inc.

[Action Items]

Action Item	Status	Responsible	Due Date
Complete DAT	Completed	Test Lab	11/16/07
Summarize DAT results	Completed	Test Lab	11/20/07
Write DAT report	In process	Test Lab	12/21/07
Provide schedule for production implementation	Rough schedule completed	Mayfield	11/23/07
Order production tooling	In process	Mayfield	05/1/08

December 12, 2007
Remington Arms Company, Inc.

[Schedule]

- Complete production tooling – Oct, 2008
- Start T&P – Nov, 2008
- Complete T&P – Dec, 2008

Declassify on: OADR
Remington Arms Company
