


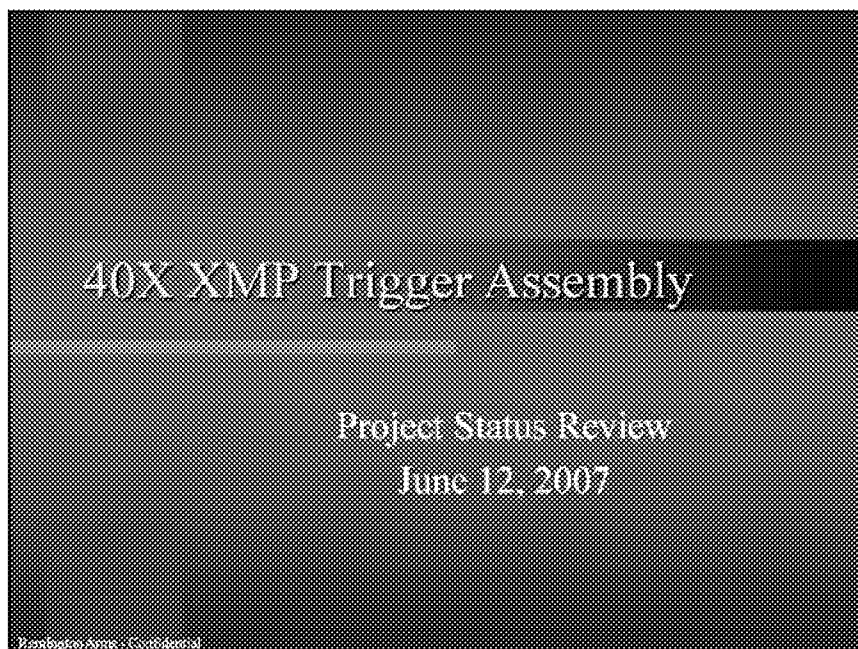

40X XMP TA Action Items

Action Item	Status	Responsible	Date
Conduct EET on 700 Varmint	Complete	Ronkainen	5/18/2007
Get parts for 700 Varmint DAT	In-process	Ronkainen	6/19/2007
Conduct DAT on 700 Varmint	Pending	R&D Test Lab	7/11/2007

Sandagun Arms - Confidential

40X XMP Status

- Rear spacer blocks sent to Ilion 6/5 for processing
- Trigger blanks sent to Ilion 6/7 for processing
- 10 of 15 guns for DAT delivered
- Production XMP parts for DAT received 6/6
- Updated primary trigger pull spring (301708) design complete and on order
- Trigger assembly drawing being updated to add right and left handed versions of the 40X XMP

Remington Arms - Confidential

40X XMP Summarized Schedule

Milestone	Date
First non-working prototype	N/A
First working prototype	N/A
EET	10/15/2006
Manufacturing involvement	3/14/2005
XR-100 DAT	4/13/2007
M/700 Varmint DAT	7/13/2007

Remington Arms - Confidential
