

February 4, 1999

Sportsman M/710

Year 2000 Introduction Development Schedule

83

Remington Arms Confidential

ET36255

M/710 Quad Chart

Confidential

Sportsman Model 710 Bolt Action Rifle

2/2/99

Lead Engineers: M. Keeney 241095

Project Description:

A bolt action rifle accommodating long action & magnum calibers; standard barrel lengths, synthetic & wood stocks; magazine box, and a reasonable grade trigger; accepts scope bases offered with optional adjustable sights.


Risk Assessment:

Medium: Due to aggressive cost and process requirements.

Project Objectives:

- Reduce cost to manufacture and manufacturing lead time.
- Above average Gross profit margin (45%).
- Offered as an entry level bolt action rifle while elevating the M/700.
- Compete directly with the Savage (111FC) similar offerings.

1999 Spending

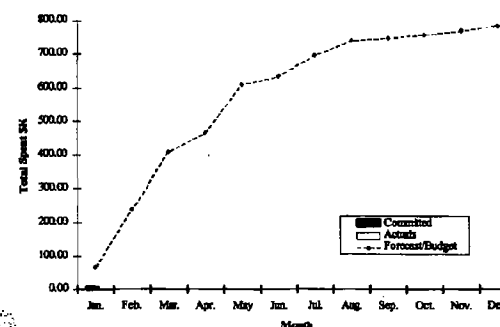

Project Milestones/Schedule:

Task Name	Finish	1999						2000	
		Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3
Sportsman M/710 (30-06)	12/3/99								
Program Approval	12/18/98								
Build EE Test - (12)	4/30/99								
EE Test	6/4/99								
Program Review - 4	8/9/99								
Final Design	8/27/99								
Build DAT Guns (40)	8/28/99								
DAT Test	8/31/99								
Design Transmittal	10/1/99								
T&P	11/1/99								
Warehouse Position	12/3/99								

Total Project Cost: Expense: \$641.51K Capital: \$340.0K

Project Status:

01/18/99

- Project Approval based on Design Review, 12/18/98
- Manufacturing cost estimate \$109.47
- Cosmetic prototype
- Schedule Development mtg with Manufacturing 01/6-7/99, limited offering year 2000
- Cosmetic Review 01/14/99, issues are barrel contour, bolt plug, and bolt handle
- Ordered components for two test assemblies, to be delivered by 2/1/99

Areas of Concern:

- Barrel processing/heat treatment
- Receiver Insert

Remington Arms Confidential

February 4, 1999

BARBER - 5.22.06r0009250

Confidential - BARBER - 5.22.06r0009250 Order Williams V. Remington

ET36256

M/710 - Status

- ★ Cosmetic Review (1/14/99)
 - Barrel (potential \$2/barrel cost savings)
 - Bolt Plug
 - Bolt Handle
- ★ Schedule Development Mtg. (1/6-7/99)
 - ◇ Development Approach
 - ◇ Schedule
 - ◇ Budget

Remington Arms Confidential

February 4, 1999

ET36257

Confidential - ~~Share~~ - 5.22.06r0009251ye Order
Williams v. Remington

M/710 Development Approach

- ★ Limited Offering – Long action only
 - 2001 magnum introduction
- ★ Parallel design and manufacturing development
 - basic bolt action design
 - program risks -- manuf. of barrel and receiver insert
 - ◇ Engineering Evaluation Testing (EET)
 - Design Acceptance Testing (DAT)
 - ◇ First pass of Trial and Pilot
 - production components

Remington Arms Confidential

February 4, 1999

ET36258

Confidential - Subject - 5.22.06r0009252 - Order

Williams v. Remington

M/710 Schedule

Task Name	Finish	1999					200
		Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr
Sportsman M/710 (30-06)	Fri 12/3/9						
Program Approval	Fri 12/18/9		12/18				
Build EE Test - (12)	Fri 4/30/9						
EE Test	Fri 6/4/9						
Program Review - 4	Wed 6/9/9			6/9			
Final Design	Fri 8/27/9						
Build DAT Guns (40)	Fri 6/25/9						
DAT Test	Tue 8/31/9						
Design Transmittal	Fri 10/1/9						
T&P	Fri 11/12/9						
Warehouse Position	Fri 12/3/9						

Remington Arms Confidential


February 4, 1999

ET36259

Confidential - Subject - 5.22.06r0009253
 Order
 Williams v. Remington

M/710 Spendout

1999 Spending

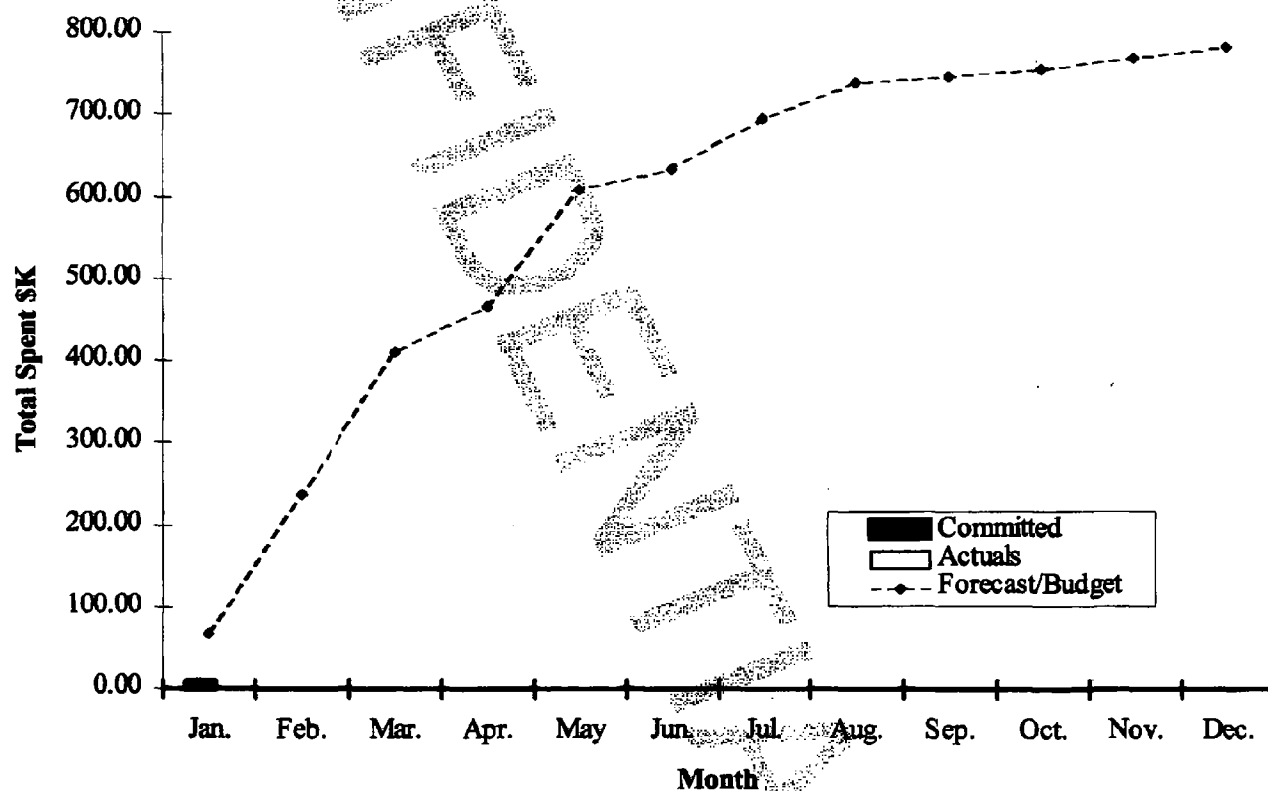

Remington Arms Confidential

February 4, 1999

ET36260

Confidential - ~~BARBER~~ - 5.22.06r0009254

Williams v. Remington

M/710 Net R&D Budget

Total Spendout \$779,775
Capital Investment - \$340,000
Net R&D Spendout **\$439,775**

Remington Arms Confidential

February 4, 1999

ET36261

Confidential - ~~Subsequent~~ - 5.22.06r0009255
Williams v. Remington

M/710 Capital Investments

- ★ Barrel Assembly Fixture \$20,000
- ★ Receiver Insert Tooling \$100,000
- ★ Bolt Plug Tooling \$55,000
- ★ Stock Tooling \$125,000
- ★ Grip Cap Tooling \$40,000

Total \$340,000

Remington Arms Confidential

February 4, 1999

ET36262

Confidential - ~~Share~~ - 5.22.06r0009256
Share - 5.22.06r0009256
Williams v. Remington

M/710 Summary

- ★ Aggressive Schedule
 - EET Program Milestone, Review 6/9/99
 - Supplier Management
 - ◇ Delivery Date Commitment
- ★ Manufacturing Priority
- ★ Non Budgeted Capital Expenditure

Remington Arms Confidential

February 4, 1999

ET36263

Confidential - Subject - 5.22.06r0009257
Shahrest Williams v. Remington
