

SPORTSMAN M/710
BOLT ACTION 241095

ID	Task Name	Start	Finish	Predecess	97	1998				1999				2000				2001					
					3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3		
1	Sportsman Model 710 Bolt Action Rifle	9/2/97	7/6/00																				
2	Program Review - III	11/17/98	12/18/98																				
3	Manufacturing Review	11/17/98	11/17/98																				
4	Re-Run Manufacturing Estimate	11/18/98	12/17/98	3																			
5	Marketing Review	12/18/98	12/18/98																				
6	Program Approval	12/23/98	12/23/98	2FS+3d																			
7	Build EE Test - Prototypes (12)	9/2/97	5/28/99																				
8	Barrel Assembly	9/2/97	9/2/97																				
9	Barrel TEST BOMBS	9/2/97	9/2/97																				
10	Receiver	9/2/97	9/2/97																				
11	Receiver Insert	9/2/97	9/2/97																				
12	Bolt Assembly	9/2/97	9/2/97																				
13	Bolt Head	9/2/97	9/2/97																				
14	Procure Components	12/28/98	5/20/99	6																			
15	Assemble Prototypes	5/21/99	5/28/99	14																			
16	EE Test	5/31/99	7/23/99																				
17	Run Test	5/31/99	7/23/99	15																			
18	Program Review - 4	7/26/99	7/26/99	17FS+1d																			
19	Final Design	5/21/99	12/23/99																				
20	Modeling	5/21/99	7/29/99	14																			
21	Detailing	7/30/99	8/12/99	20																			

Project: Sportsman M/710 Bolt Action
Project Code: 241095
Date: 1/6/99

Task

Progress

Milestone


Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

\\ERDNTAS1\241095\241095TL.MPP

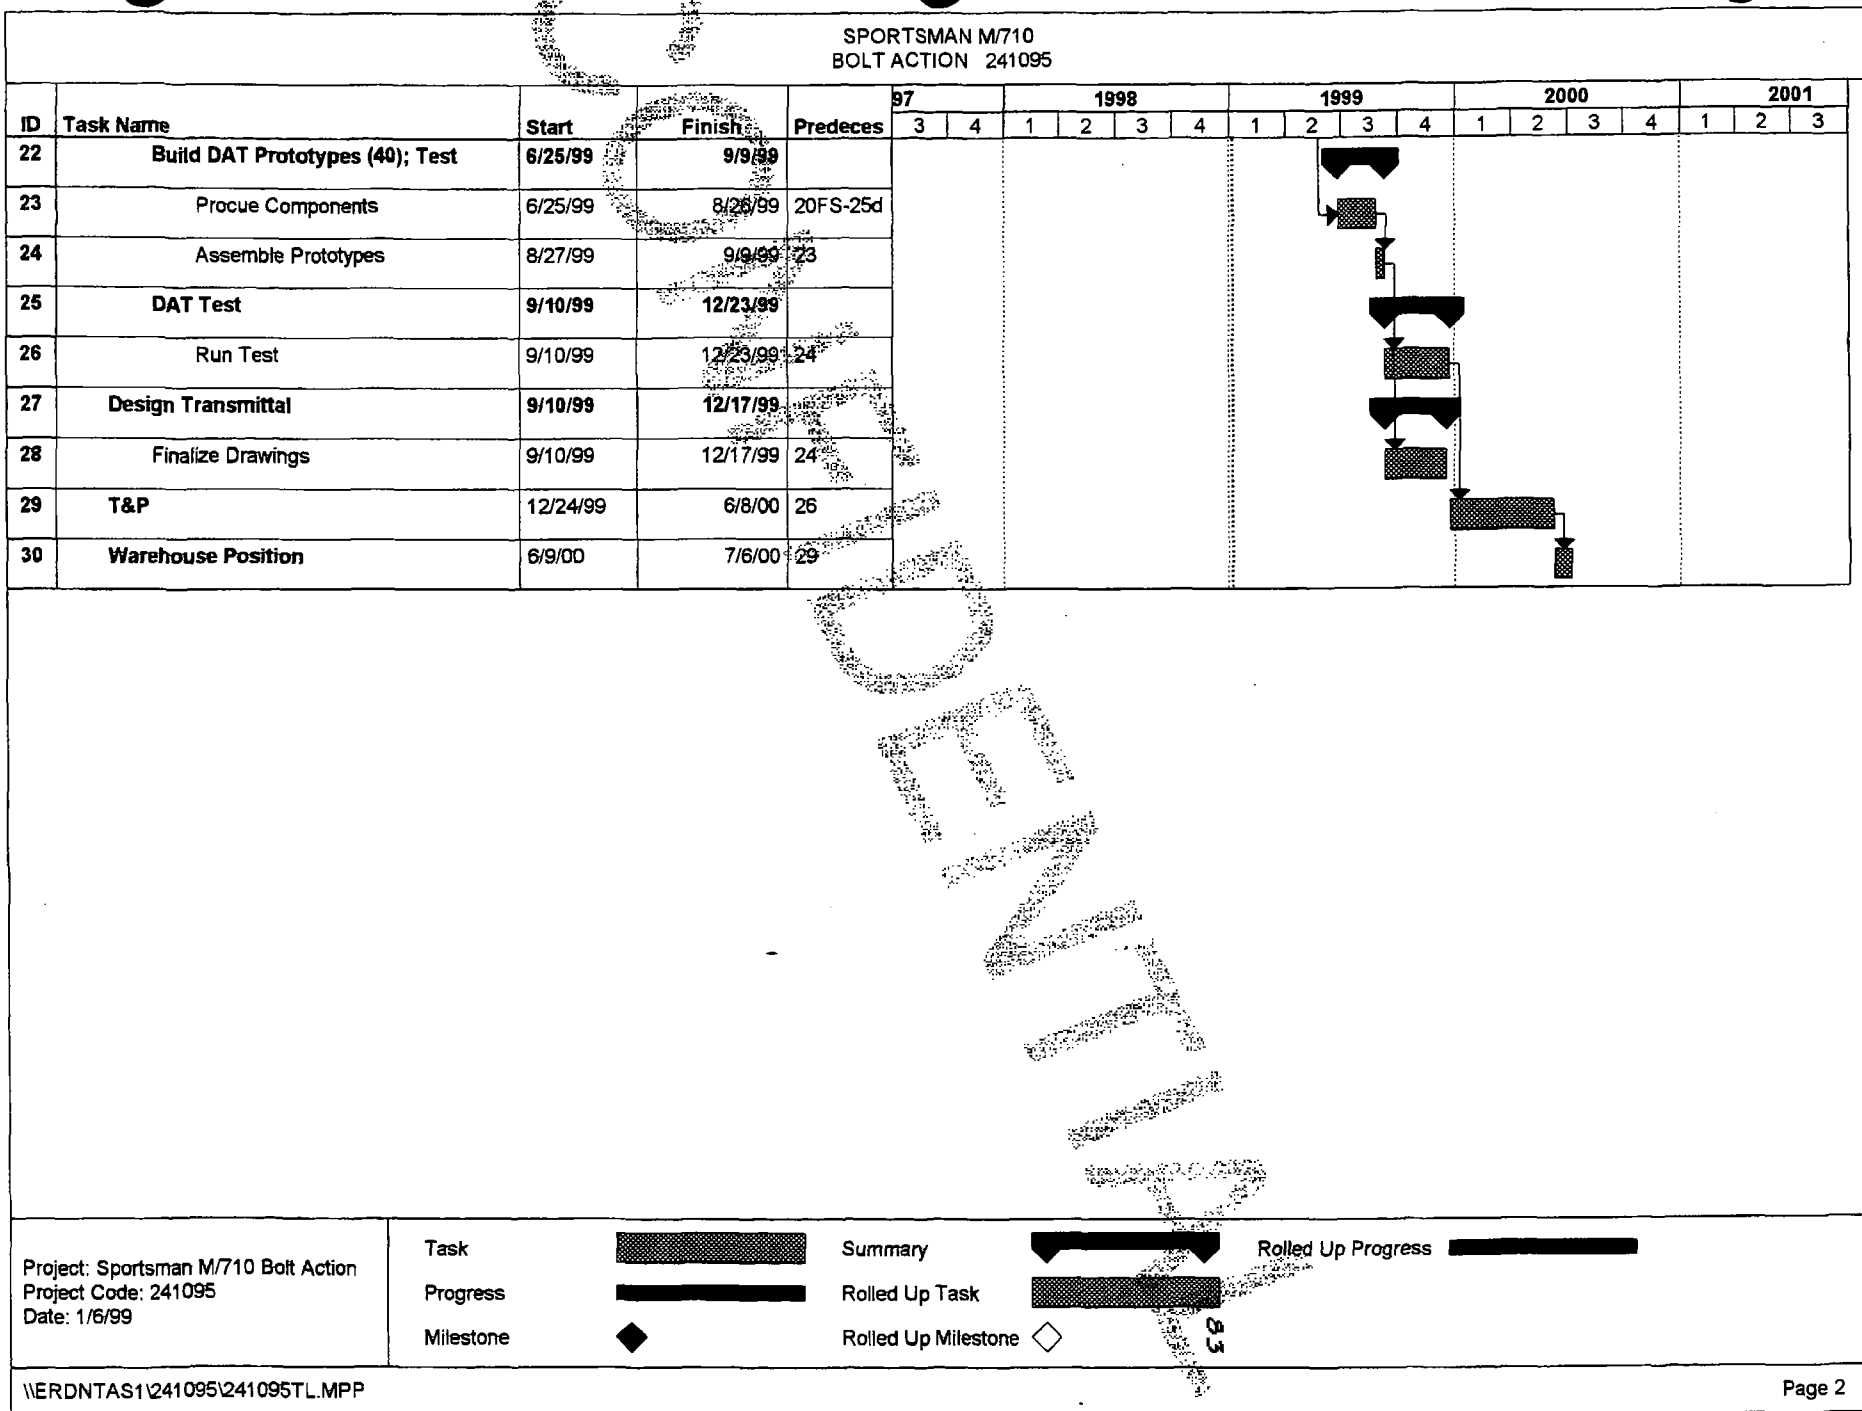

ET36279

Confidential - Subject - 5.22.06r0009273 Order

Williams V. Remington
